

La Habra City School District

Measure "O" – Bond Program Update


October 9, 2013

Measure "O" Overview

- In July 2012, the Board adopted a Facilities Assessment & Implementation plan that identified a facilities improvement strategy over four phases beginning in 2013 and ending in 2025
- The Plan prescribed four project categories to be implemented during the first phase of program implementation, between 2013-2016:
 - 1. Academy upgrades at Washington and Imperial middle schools
 - 2. Technology upgrades, including mobile computing devices, wireless network enhancements, and modern telephone systems
 - 3. Roofing repair and replacement at critical locations
 - 4. Improved energy efficiency and deferred maintenance
- In November 2012, La Habra voters approved funding this plan through Measure "O", providing \$31 million in General Obligation bond authorization over time toward planned improvements
- Implementation planning began with Projects 1 and 2 immediately following the bond's passage; a bid for Project 3 was awarded in May 2013 and construction has been underway throughout the summer; preliminary planning for Project 4 improvements may be launched concurrently with ongoing work
- This presentation provides an overview of progress to date on implementing these Measure "O" improvements

Measure "O" Community Website

- A Measure "O" website has been provided as a community resource for information about the facilities implementation program
- Visitors can peruse information on project updates, view photos of construction activity, or learn about the Facilities Assessment & Implementation Plan that guides the process
- A section also provides resources on the Citizens' Oversight Committee, including presentations, expenditure reports, and meeting minutes, in compliance with Prop. 39 requirements



http://www.LaHabraMeasureO.org

Project 1: Academy Improvements

- Project 1 refers to all work to upgrade Washington MS and Imperial MS in order to provide academy learning environments
- Components that do not require new extended approval by the Division of the State Architect (DSA) have moved forward throughout the summer of 2013:
 - Electronic marquees (signs)
 - Courtyard safety improvements at Imperial MS
 - Selection and order of modern furnishings

Proj 1: Courtyard Safety & Entry Marquees

- At its July 25th meeting the Board awarded a bid to Minco Construction for installation of electronic marquees at both middle schools and construction of courtyards at Imperial Middle School
- The program team has confirmed the final design of electronic marquees for each site, construction of utility connections for the marquees has been completed, and manufacturing of the digital displays is underway
- Reconstruction of the east and west courtyards at Imperial Middle School is underway
 to provide improved safety and a more usable space for outdoor activity
- Courtyard excavation revealed underground conduits that necessitate a three foot setback between planters and covered walkways; CFW is reviewing proposed change orders with District staff to ensure minimum use of project contingency
- Drawings by TDM Architects, Inc. are provided on the following slides






Under construction Fall 2013

Marquee at Washington Middle School






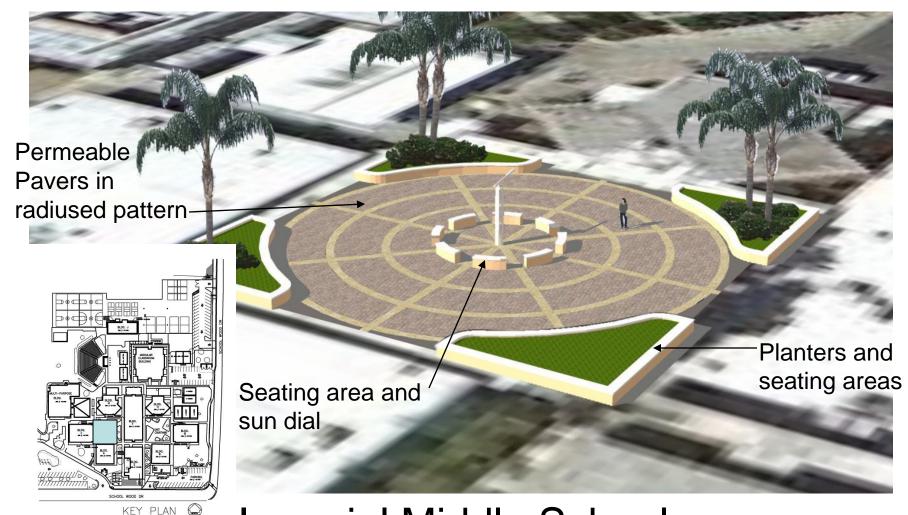







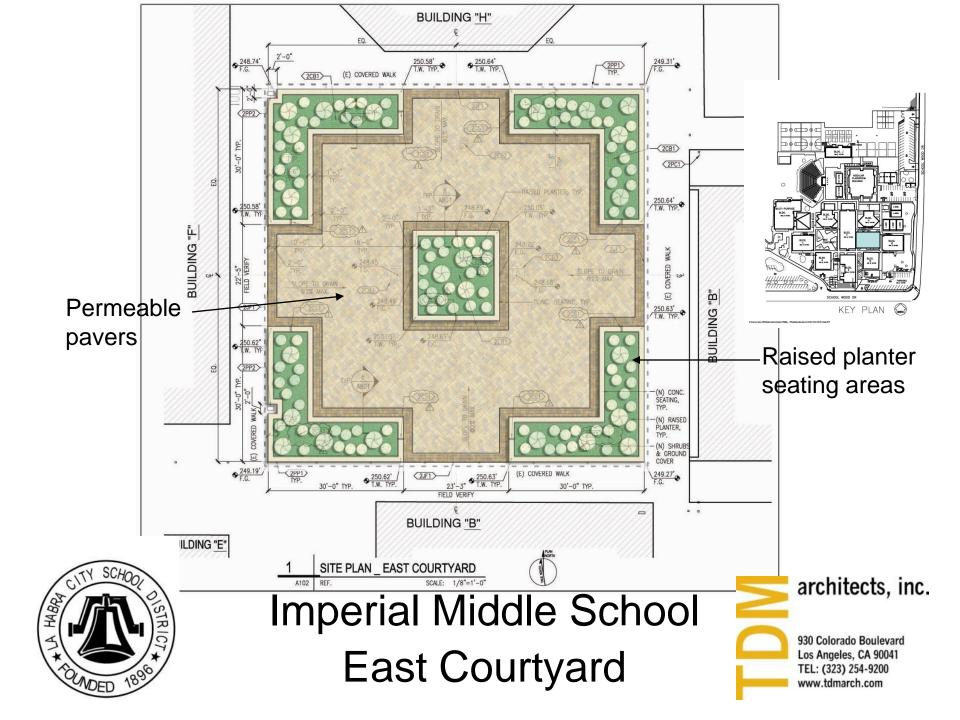


Imperial Middle School Courtyards under construction












Program Signage


 Project information signage will be installed at Washington & Imperial Middle Schools to increase community awareness of Measure "O" implementation and progress

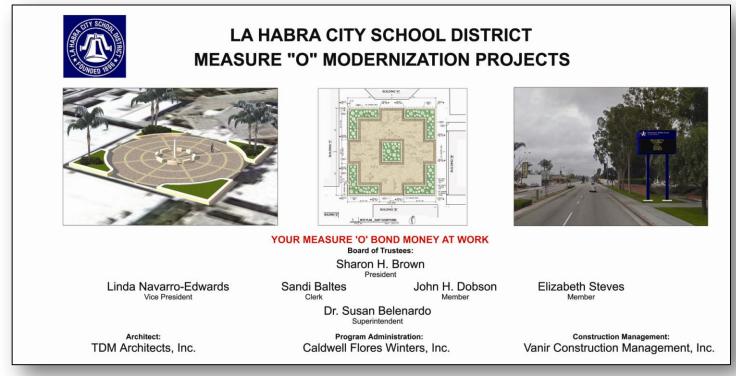



Proj 1: Furnishings


- District staff completed an evaluation of furniture options and CFW has proceeded with coordinating vendor orders with District purchasing
- New furnishings will be evaluated at both middle schools and considered for subsequent orders as Project 1 construction at the middle schools proceeds

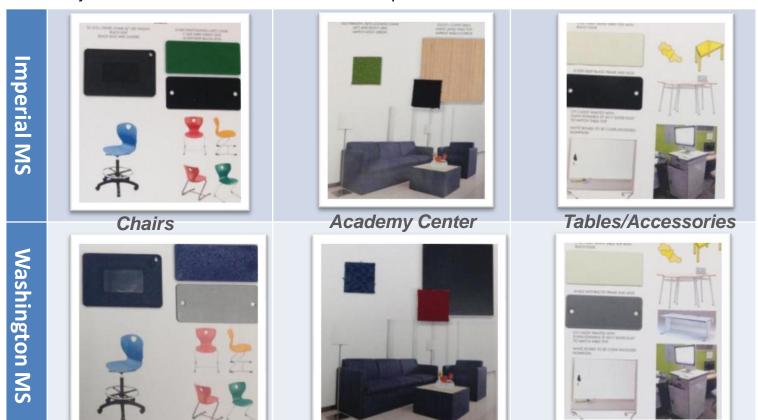

Proj 1: Spring/Summer 2014 Construction


- Components that require an approval process with DSA recently completed "Schematic Design" and now moving through "Design Development":
 - Washington Middle School Classroom/Academy Center modernization
 - Imperial Middle School Classroom/Academy Center modernization
- Pending timely review and approval of these improvements by DSA, the program schedule calls for physical construction work to commence during the District's 2014 spring recess
- Construction of interior spaces has been scheduled for completion by the start of the 2014-15 academic year
- Site principals participated in discussions regarding the scheduled construction in order to plan ahead at the start of the 2013-14 academic year
- The District's testing and inspection firm will be on hand once construction begins to inspect general contractor's work for compliance with the plans, specification and State code; American Engineering Laboratories, Inc., was approved by the Board as the District's Inspector of Record (IOR) on July 25th
- Drawings by TDM Architects, Inc. are provided on the following slides

Washington Middle School Building E Modernization

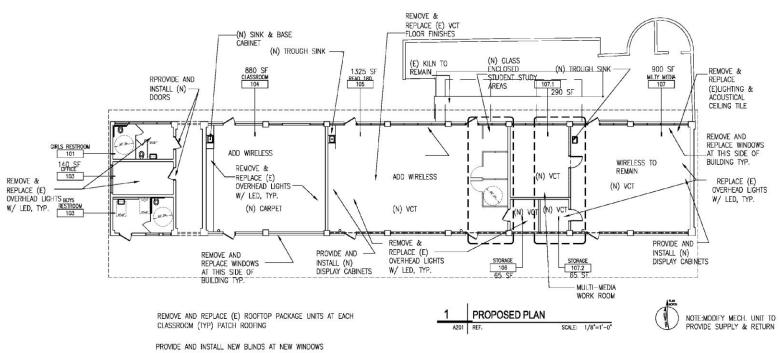



PREP AND REPAINT ALL INTERIORS





Washington Middle School Classroom Modernization at Bldg J



Modernization typical at all classrooms this building



930 Colorado Boulevard Los Angeles, CA 90041 TEL: (323) 254-9200 www.tdmarch.com

KEY PLAN 👄

Washington Middle School Classroom Modernization at Bldg J



classrooms this building



architects, inc.

930 Colorado Boulevard Los Angeles, CA 90041 TEL: (323) 254-9200 www.tdmarch.com

KEY PLAN O

Project 2: Technology Improvements

- The District has completed ordering, setup, and deployment to school sites for over 2,000 iPads to date
 - Devices are setup with Griffin "Survivor" cases to secure and protect the iPad from accidental damage as well as preloaded with productivity and educational apps
 - Mobile charging carts allow for a classroom set of devices to be wheeled between rooms as well as keep all devices secure and fully charged for student and teacher use
 - Teachers are completing professional development courses prior to introducing iPads into the curriculum in order to ensure devices are used effectively as instructional tools
- On July 18th the Board approved a lease contract with Cisco Systems to provide the installation of modern telephone systems, wireless network equipment, and required server infrastructure, funded in part by Measure "O" dollars
- Federal E-rate program contributions to cabling and wireless upgrades are still pending



Proj 3: Roofing Improvements

Surveys of roofing conditions throughout the District identified the following sites and buildings for initial roofing work to be completed during the summer of 2013:

School	Building	Roof Area
Imperial M S	Bldg A (Admin/Library)	6,090
	Bldg G (Sci Lab)	3,800
	Bldg K (MPR, Kitchen, Music)	9,304
Washington M S	Bldg B (Admin/MPR)	9,418
	Bldg G (Computers/Home Ec)	4,100
	Bldg H (Music/Shop)	5,094
Las Lomas E S	Bldg C (Library)	5,100
	Bldg E (MPR/Kitchen)	4,455
	Bldg D (Admin) mechanical well &	
Las Positas E S	Covered Walkway	800
Ladera Palma E S	Bldg D (Admin)	4,000
	TOTAL AREA	52,161

 Construction of new roofing is now largely finished; final inspections and "punch" lists are being completed to determine remaining work that the contractor must perform under contract



Master Budget Overview

		Measure "O"	Measure "K"	Country Colored	
		G.O. Bond	G.O. Bond	County School	
Project		(Fund 24)	(Funds 21-23)	Facilities (Fund 35)	Total
mperial Middle School					
Science Labs		\$156,477	\$0	\$0	\$156,477
Campus Entry		\$142,051	\$0	\$0	\$142,051
Academy Center		\$726,685	\$0	\$0	\$726,685
Classroom Improvements		\$76,223	\$0	\$0	\$76,223
Safety & Courtyards		\$297,029	\$0	\$0	\$297,029
	Total	\$1,398,465	\$0	\$0	\$1,398,465
Vashington Middle School					
Drop-Off		\$103,457	\$0	\$0	\$103,457
Classroom Improvements		\$416,883	\$0	\$0	\$416,883
Academy Center		\$743,637	\$0	\$0	\$743,637
Site Outdoor Lighting		\$45,504	\$0	\$0	\$45,504
Campus Entry		\$136,866	\$0	\$0	\$136,866
Kitchen Lighting		\$12,520	\$0	\$0	\$12,520
	Total	\$1,458,867	\$0	\$0	\$1,458,867
Districtwide					
Technology					
Equipment		\$842,952	\$0	\$0	\$842,952
Wiring		\$280,000	\$0	\$0	\$280,000
Lease payments		\$634,000	\$0	\$0	\$634,000
Roofing		\$458,270	\$404,898	\$0	\$863,168
Deferred Maintenance & Energy Management		\$614,535	\$0	\$464,399	\$1,078,935
	Total	\$2,829,757	\$404,898	\$464,399	\$3,699,054
Program Reserve					
Program Reserve		\$588,336	\$0	\$0	\$588,336
	Total	\$588,336	\$0	\$0	\$588,336
GRAND TOTAL		\$6,275,425	\$404,898	\$464,399	\$7,144,722

Program Expenditures (July 1, 2012-September 15, 2013)

		Fiscal Yea	nditures)	
Project	Budget	2012 - 2013	2013 - 2014	Total
Imperial Middle School				_
Science Labs				
Total	\$156,477	\$7,675	\$3,839	\$11,514
Campus Entry				
Total	\$142,051	\$8,686	\$3,914	\$12,601
Academy Center	4	4.000	4	<u> </u>
Total	\$726,685	\$40,582	\$16,238	\$56,820
Classroom Improvements	ά π ς 222	<u> </u>	<u> </u>	
Total	\$76,223	\$8,689	\$1,841	\$10,529
Safety & Courtyards	¢207.020	¢1C 244	¢22.505	¢20.040
Total	\$297,029 \$1,398,465	\$16,344	\$22,696	\$39,040 \$130,504
Imperial Middle School Total Washington Middle School	\$1,398,465	\$81,976	\$48,528	\$130,304
Drop-Off				
Total	\$103,457	\$5,034	\$2,613	\$7,646
Classroom Improvements	7103,437	75,054	72,013	у 7,0 4 0
Total	\$416,883	\$15,748	\$10,765	\$26,513
Academy Center	ψ 110,000	Ψ10,7 10	φ10,703	Ψ20/313
Total	\$743,637	\$25,598	\$17,357	\$42,955
Site Outdoor Lighting	. , , -	, , , , , ,	. ,	
Total	\$45,504	\$4,953	\$2,620	\$7,573
Campus Entry	· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·		<u> </u>
Total	\$136,866	\$3,193	\$2,077	\$5,270
Kitchen Lighting				
Total	\$12,520	\$629	\$8,915	\$9,545
Washington Middle School Total	\$1,458,867	\$55,154	\$44,347	\$99,501

Program Expenditures (July 1, 2012-September 15, 2013)

		Fiscal Year Actuals (Expenditures)			
	Budget	2012 - 2013	2013 - 2014	Total	
		-		·	
Total	\$1,756,952	\$842,952	\$317,754	\$1,160,706	
Total	\$863,168	\$509,039	\$185,892	\$694,931	
Energy Manageme	nt	-			
Total	\$1,078,935	\$38,700	\$13,995	\$52,695	
Districtwide Total	\$3,699,054	\$1,390,691	\$517,640	\$1,908,332	
	\$588,336				
	\$7,144,722	\$1,527,821	\$610,515	\$2,138,336	
	Total Energy Manageme Total	Total \$1,756,952 Total \$863,168 Energy Management Total \$1,078,935 Districtwide Total \$3,699,054 \$588,336	Total \$1,756,952 \$842,952 Total \$863,168 \$509,039 Energy Management Total \$1,078,935 \$38,700 Districtwide Total \$3,699,054 \$1,390,691	Total \$1,756,952 \$842,952 \$317,754 Total \$863,168 \$509,039 \$185,892 Energy Management Total \$1,078,935 \$38,700 \$13,995 Districtwide Total \$3,699,054 \$1,390,691 \$517,640	

*Notes:

- 1 Total expenditures for Measure "O" and Measure "K" from July 1, 2012 to September 15, 2013 is \$2,677,354
- 2 Total program expenditures reported above exclude other non-program related expenses (e.g., cost of issuance, county election costs, and other non-program expenses totaling \$539,018)

The Look Ahead



- The Citizens' Oversight Committee (COC) will meet October 9th to review the included expenditure reports; under its purview the BOC evaluates these expenditures' consistency with Measure "O"
- Design Development is currently underway and expected to be approved by October 15th
- Printing and placement of Measure "O" program signage, installation of Permanent Electronic Marquees, and completion of courtyard work will occur by November 1st
- Construction Documents are to be complete and approved by November 15th in preparation for DSA submittal
- Approval of plans by the Division of the State Architect (DSA) is expected by March 1st, 2014
- Bidding for spring/summer 2014 work is planned to conclude and be Board approved by March 13th, 2014
- Construction at Washington and Imperial MS is targeted to begin during the spring of 2014 and be complete by fall 2014

Appendix: Detailed Expenditure Report

LA HABRA CITY SCHOOL DISTRICT						
Program Expenditures Report (as of September 15, 2013) Fiscal Year Actuals (Expenditures)						
Project	Budget	Object Code	Fiscal Year Actua 2012 - 2013	ls (Expenditures) 2013 - 2014	Total	
rioject	Buuget	Object code	2012 - 2013	2013 - 2014	TOLAI	
mperial Middle School						
Science Labs						
Consultng/ProfSvs & Operating		5800				
Program Manager			\$4,944	\$824	\$5,768	
Construction Management			\$0	\$0	\$0	
Labor Compliance Program			\$0	\$0	\$0	
Moving & Storage			\$0	\$0	\$0	
Operating Expense-Advertising		5806	\$583	\$71	\$654	
Operating Expense-Legal		5809	\$269	\$0	\$269	
Bldgs & Improvement Buildings		6200	\$112	\$0 \$0	\$112	
Construction		6258	\$0 \$0	\$0 \$2.044	\$0	
Architect Fees DSA Plan Check Fees		6260 6262	\$0 \$0	\$2,944 \$0	\$2,944 \$0	
Preliminary Tests		6265	\$0 \$0	\$0 \$0	\$0 \$0	
Other Planning Costs		6266	\$1,768	\$0 \$0	\$1,768	
Inspection (Construction)		6290	\$1,768	\$0 \$0	\$1,700	
Total	\$156,477	0230	\$7.675	\$3,839	\$11,514	
Campus Entry	,,		Ţ.,O.O	+-,555	T-2,027	
Consultng/ProfSvs & Operating		5800				
Program Manager			\$5,092	\$817	\$5,909	
Construction Management			\$0	\$0	\$0	
Labor Compliance Program			\$0	\$0	\$0	
Operating Expense-Advertising		5806	\$529	\$64	\$593	
Operating Expense-Legal		5809	\$244	\$0	\$244	
Bldgs & Improvement Buildings		6200	\$102	\$0	\$102	
Construction		6258	\$0	\$0	\$0	
Architect Fees		6260	\$0	\$3,033	\$3,033	
DSA Plan Check Fees		6262	\$0	\$0	\$0	
Preliminary Tests		6265	\$0	\$0	\$0	
Other Planning Costs		6266	\$2,719	\$0 \$0	\$2,719	
Inspection (Construction) Total	\$142,051	6290	\$0 \$8,686	\$0 \$3,914	\$0 \$12,601	
Academy Center	\$142,031		30,000	\$5,914	\$12,001	
Consulting/ProfSvs & Operating		5800				
Program Manager		3000	\$20,724	\$3,576	\$24,300	
Construction Management			\$0	\$0	\$0	
Labor Compliance Program			\$0	\$0	\$0	
Moving & Storage			\$0	\$0	\$0	
Operating Expense-Advertising		5806	\$2,707	\$329	\$3,036	
Operating Expense-Legal		5809	\$1,248	\$0	\$1,248	
Bldgs & Improvement Buildings		6200	\$520	\$0	\$520	
Construction		6258	\$0	\$0	\$0	
Architect Fees		6260	\$0	\$12,334	\$12,334	
DSA Plan Check Fees		6262	\$0	\$0	\$0	
Preliminary Tests		6265	\$0	\$0	\$0	
Other Planning Costs		6266	\$15,382	\$0	\$15,382	
Inspection (Construction)		6290	\$0	\$0 \$0	\$0	
Instructional Equipment/Furniture	\$726,685	7619	\$0	\$0 \$16,238	\$0 \$56,820	
Classroom Improvements	5720,085		\$40,582	\$10,238	აახ,820	
Classroom Improvements Consultng/ProfSvs & Operating		5800				
Program Manager		3000	\$2,375	\$396	\$2,772	
Construction Management			\$2,373 \$0	\$390 \$0	\$2,772	
Labor Compliance Program			\$0	\$0	\$0 \$0	
Moving & Storage			\$0	\$0	\$0 \$0	
Operating Expense-Advertising		5806	\$284	\$34	\$318	
Operating Expense-Legal		5809	\$131	\$0	\$131	
Bldgs & Improvement Buildings		6200	\$55	\$0	\$55	
Construction		6258	\$0	\$0	\$0	
Architect Fees		6260	\$0	\$1,410	\$1,410	
DSA Plan Check Fees		6262	\$0	\$0	\$0	
Preliminary Tests		6265	\$0	\$0	\$0	
Other Planning Costs		6266	\$5,844	\$0	\$5,844	
Inspection (Construction)		6290	\$0	\$0	\$0	
	\$76,223	1	\$8,689	\$1,841	\$10,529	

			Fiscal Voar Actua	ls (Expenditures)	
Project	Budget	Object Code	2012 - 2013	2013 - 2014	Total
Safety & Courtyards		and the second	2025		
Materials and Supplies		4300	\$0	\$3,580	\$3,580
Consultng/ProfSvs & Operating		5800			
Program Manager			\$5,092	\$1,081	\$6,173
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0	\$0	\$0
Operating Expense-Advertising		5806	\$1,107	\$134	\$1,241
Operating Expense-Legal		5809	\$510	\$0	\$510
Bldgs & Improvement Buildings		6200	\$212	\$0	\$212
Construction (Contractor)		6256	\$7,600	\$14,868	\$22,468
Construction		6258	\$0	\$0	\$0
Architect Fees		6260	\$0	\$3,033	\$3,033
DSA Plan Check Fees		6262	\$0	\$0	\$0
Preliminary Tests		6265	\$0	\$0	\$0
Other Planning Costs		6266	\$1,823	\$0	\$1,823
Inspection (Construction)	¢207.020	6290	\$0	\$0	\$0
Total	\$297,029		\$16,344	\$22,696	\$39,040
Imperial Middle School Total \$ Washington Middle School	1,398,465		\$81,976	\$48,528	\$130,504
Drop-Off		 			
Consultng/ProfSvs & Operating		5800			
Program Manager		3000	\$3,207	\$537	\$3,744
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0 \$0	\$0	\$0
Operating Expense-Advertising		5806	\$369	\$47	\$416
Operating Expense-Legal		5809	\$178	\$0	\$178
Bldgs & Improvement Buildings		6200	\$71	\$ 0	\$71
Construction		6258	\$0	\$0	\$0
Architect Fees		6260	\$0	\$2,015	\$2,015
DSA Plan Check Fees		6262	\$0	\$0	\$0
Preliminary Tests		6265	\$0	\$0	\$0
Other Planning Costs		6266	\$1,209	\$14	\$1,223
Inspection (Construction)		6290	\$0	\$0	\$0
Total	\$103,457		\$5,034	\$2,613	\$7,646
Classroom Improvements					
Consultng/ProfSvs & Operating		5800			
Program Manager			\$13,257	\$2,204	\$15,461
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0	\$0	\$0
Moving & Storage		=	\$0	\$0	\$0
Operating Expense-Advertising		5806	\$1,489	\$188	\$1,677
Operating Expense-Legal		5809	\$716	\$0 \$0	\$716
Bldgs & Improvement Buildings Construction		6200 6258	\$286 \$0	\$0 \$0	\$286 \$0
Architect Fees		6260	\$0 \$0	\$0 \$8,316	\$0 \$8,316
DSA Plan Check Fees		6262	\$0 \$0	\$8,316 \$0	\$8,316 \$0
Preliminary Tests		6265	\$0 \$0	\$0 \$0	\$0 \$0
Other Planning Costs		6266	\$0 \$0	\$57	\$0 \$57
Inspection (Construction)		6290	\$0 \$0	\$37 \$0	\$37 \$0
Total	\$416,883	0230	\$15,748	\$10,765	\$26,513
Academy Center	, -,		, ==,: .0	,,	
Consultng/ProfSvs & Operating		5800			
Program Manager			\$21,155	\$3,652	\$24,807
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0	\$0	\$0
Moving & Storage			\$0	\$0	\$0
Operating Expense-Advertising		5806	\$2,656	\$336	\$2,992
Operating Expense-Legal		5809	\$1,277	\$0	\$1,277
Bldgs & Improvement Buildings		6200	\$510	\$0	\$510
Construction		6258	\$0	\$0	\$0
Architect Fees		6260	\$0	\$13,268	\$13,268
DSA Plan Check Fees		6262	\$0	\$0	\$0
Preliminary Tests		6265	\$0	\$0	\$0
Other Planning Costs		6266	\$0	\$101	\$101
		1	4.0	40	ćo
Inspection (Construction)	į.	6290	\$0	\$0	\$0
Inspection (Construction) Instructional Equipment/Furniture		6290 7619	\$0 \$0	\$0 \$0	\$0 \$0

			Fiscal Year Actua	ls (Expenditures)	
Project	Budget	Object Code	2012 - 2013	2013 - 2014	Total
Site Outdoor Lighting					
Consultng/ProfSvs & Operating		5800			
Program Manager			\$3,400	\$461	\$3,861
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0	\$0	\$0
Operating Expense-Advertising		5806	\$163	\$21	\$183
Operating Expense-Legal		5809	\$78	\$0	\$78
Bldgs & Improvement Buildings		6200	\$31	\$0	\$31
Construction		6258	\$0	\$0	\$0
Architect Fees		6260	\$0	\$2,132	\$2,132
DSA Plan Check Fees		6262	\$0	\$0	\$0
Other Planning Costs		6266	\$1,281	\$6	\$1,287
Inspection (Construction)		6290	\$0	\$0	\$0
Total	\$45,504		\$4,953	\$2,620	\$7,573
Campus Entry					
Consultng/ProfSvs & Operating		5800			
Program Manager			\$2,375	\$502	\$2,877
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0	\$0	\$0
Operating Expense-Advertising		5806	\$489	\$62	\$551
Operating Expense-Legal		5809	\$235	\$0	\$235
Bldgs & Improvement Buildings		6200	\$94	\$0	\$94
Construction		6258	\$0	\$0	\$0
Architect Fees		6260	\$0	\$1,494	\$1,494
DSA Plan Check Fees		6262	\$0	\$0	\$0
Preliminary Tests		6265	\$0	\$0	\$0
Other Planning Costs		6266	\$0	\$19	\$19
Inspection (Construction)		6290	\$0	\$0	\$0
Total	\$136,866		\$3,193	\$2,077	\$5,270
Kitchen Lighting					
Consultng/ProfSvs & Operating		5800			
Program Manager			\$401	\$66	\$467
Construction Management			\$0	\$0	\$0
Labor Compliance Program			\$0	\$0	\$0
Operating Expense-Advertising		5806	\$45	\$6	\$50
Operating Expense-Legal		5809	\$22	\$0	\$22
Bldgs & Improvement Buildings		6200	\$9	\$0	\$9
Construction		6258	\$0	\$8,584	\$8,584
Architect Fees		6260	\$0	\$257	\$257
DSA Plan Check Fees		6262	\$0	\$0	\$0
Other Planning Costs		6266	\$154	\$2	\$155
Inspection (Construction)	410.500	6290	\$0	\$0	\$0
Total	\$12,520		\$629	\$8,915	\$9,545
Washington Middle School Total	\$1,458,867		\$55,154	\$44,347	\$99,501
Districtwide					
Technology Equipment					
Equipment		7610	¢042.0E2	\$0	¢042.0E2
Instructional Equipment/Furniture Total	\$842,952	7619	\$842,952 \$842,952	\$0 \$0	\$842,952 \$842,952
Wiring	2044,534	1	255,240ب	ŞU	عرب42,334 م
		1			
Construction		6258	¢n	Ċn	ĊΛ
Construction	\$280,000	6258	\$0 \$0	\$0 \$0	\$0 \$0
Total	\$280,000	6258	\$0 \$0	\$0 \$0	\$0 \$0
Total Lease payments	\$280,000		\$0	\$0	\$0
Total Lease payments Other Debt Service - Interest	\$280,000	7438	\$0 \$0	\$0 \$3,722	\$0 \$3,722
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal			\$0 \$0 \$0	\$0 \$3,722 \$314,031	\$0 \$3,722 \$314,031
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total	\$634,000	7438	\$0 \$0 \$0 \$0	\$0 \$3,722 \$314,031 \$317,754	\$0 \$3,722 \$314,031 \$317,754
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Total		7438	\$0 \$0 \$0	\$0 \$3,722 \$314,031	\$0 \$3,722 \$314,031
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing	\$634,000	7438 7439	\$0 \$0 \$0 \$0	\$0 \$3,722 \$314,031 \$317,754	\$0 \$3,722 \$314,031 \$317,754
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Total Roofing Consultng/ProfSvs & Operating	\$634,000	7438	\$0 \$0 \$0 \$0 \$0 \$842,952	\$0 \$3,722 \$314,031 \$317,754 \$317,754	\$3,722 \$314,031 \$317,754 \$1,160,706
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Total Roofing Consultng/ProfSvs & Operating Program Manager	\$634,000	7438 7439	\$0 \$0 \$0 \$0 \$0 \$842,952	\$0 \$3,722 \$314,031 \$317,754 \$317,754	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program	\$634,000	7438 7439 5800	\$0 \$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$34,394 \$0
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising	\$634,000	7438 7439 5800	\$0 \$0 \$0 \$0 \$29,587 \$0 \$919	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$34,394 \$0 \$1,310
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal	\$634,000	7438 7439 5800 5806 5809	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$34,394 \$0 \$1,310 \$1,483
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal Hazardous Materials	\$634,000	7438 7439 5800 5806 5809 5813	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483 \$0	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0 \$1,050	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$34,394 \$0 \$1,310 \$1,483 \$1,050
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal Hazardous Materials Roofing - Deferred Maintenance	\$634,000	7438 7439 5800 5806 5809 5813 6202	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483 \$0 \$473,680	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0 \$1,050 \$173,920	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$34,394 \$0 \$1,310 \$1,483 \$1,050 \$647,600
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal Hazardous Materials Roofing - Deferred Maintenance Construction	\$634,000	7438 7439 5800 5806 5809 5813 6202 6258	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483 \$0 \$473,680 \$0	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0 \$1,050 \$173,920 \$0	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$1,310 \$1,483 \$1,050 \$647,600 \$0
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal Hazardous Materials Roofing - Deferred Maintenance Construction Architect Fees	\$634,000	7438 7439 5800 5806 5809 5813 6202 6258 6260	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483 \$0 \$473,680 \$0 \$0	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0 \$1,050 \$173,920 \$0 \$5,725	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$1,310 \$1,483 \$1,050 \$647,600 \$0 \$5,725
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal Hazardous Materials Roofing - Deferred Maintenance Construction Architect Fees Preliminary Tests	\$634,000	7438 7439 5800 5806 5809 5813 6202 6258 6260 6265	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483 \$0 \$473,680 \$0 \$0 \$3,370	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0 \$1,050 \$173,920 \$0 \$5,725 \$0	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$1,310 \$1,483 \$1,050 \$647,600 \$0 \$5,725 \$3,370
Total Lease payments Other Debt Service - Interest Other Debt Service - Principal Total Roofing Consultng/ProfSvs & Operating Program Manager Labor Compliance Program Operating Expense-Advertising Operating Expense-Legal Hazardous Materials Roofing - Deferred Maintenance Construction Architect Fees	\$634,000	7438 7439 5800 5806 5809 5813 6202 6258 6260	\$0 \$0 \$0 \$0 \$842,952 \$29,587 \$0 \$919 \$1,483 \$0 \$473,680 \$0 \$0	\$0 \$3,722 \$314,031 \$317,754 \$317,754 \$4,807 \$0 \$390 \$0 \$1,050 \$173,920 \$0 \$5,725	\$0 \$3,722 \$314,031 \$317,754 \$1,160,706 \$1,310 \$1,483 \$1,050 \$647,600 \$0 \$5,725

				Fiscal Year Actua	Is (Expenditure:	s)
oject		Budget	Object Code	2012 - 2013	2013 - 2014	Total
Deferred Maintenance & Energy N	1anagement					
Consultng/ProfSvs & Operating		5800				
Program Man	ager			\$36,847	\$5,989	\$42,835
Labor Complic	nce Program			\$0	\$0	\$0
Operating Expense-Ad	dvertising		5806	\$0	\$488	\$488
Operating Expense-Le	gal		5809	\$1,853	\$0	\$1,853
Bldgs & Improvement	Buildings		6200	\$0	\$7,519	\$7,519
Construction			6258	\$0	\$0	\$0
DSA Plan Check Fees			6262	\$0	\$0	\$0
Preliminary Tests			6265	\$0	\$0	\$0
Inspection (Construct	ion)		6290	\$0	\$0	\$0
	Total	\$1,078,935		\$38,700	\$13,995	\$52,695
Distric	twide Total	\$3,699,054		\$1,390,691	\$517,640	\$1,908,332
gram Reserve						
Program Reserve		\$588,336				
RAND TOTAL		\$7,144,722		\$1,527,821	\$610,515	\$2,138,336

*Notes:

- 1 Total expenditures for Measure "O" and Measure "K" from July 1, 2012 to September 15, 2013 is \$2,677,354 2 Total program expenditures reported above exclude other non-program related expenses (e.g., cost of issuance, county election costs, and other non-program expenses totaling \$539,018)
